



# Infrastructure Recovery Daily Report


Friday, November 6, 2015

## Resources Deployed

SCDOT Maintenance forces have led the majority of the repairs, including initiating 3 bridge replacement projects with in-house forces.

Road and Bridge Contractors will be engaged as needed. Currently, 23 Highway/Bridge Contractors have been engaged to assist with 65 different "emergency/spot repairs" in 16 counties. Contractors have also been engaged on 10 bridge replacement or major bridge/culvert repair projects in 4 counties. 21 of the firms are SC firms, 1 GA firm, 1 NC firm, and 4 of the firms are DBEs.

## Closures on the State-Maintained System

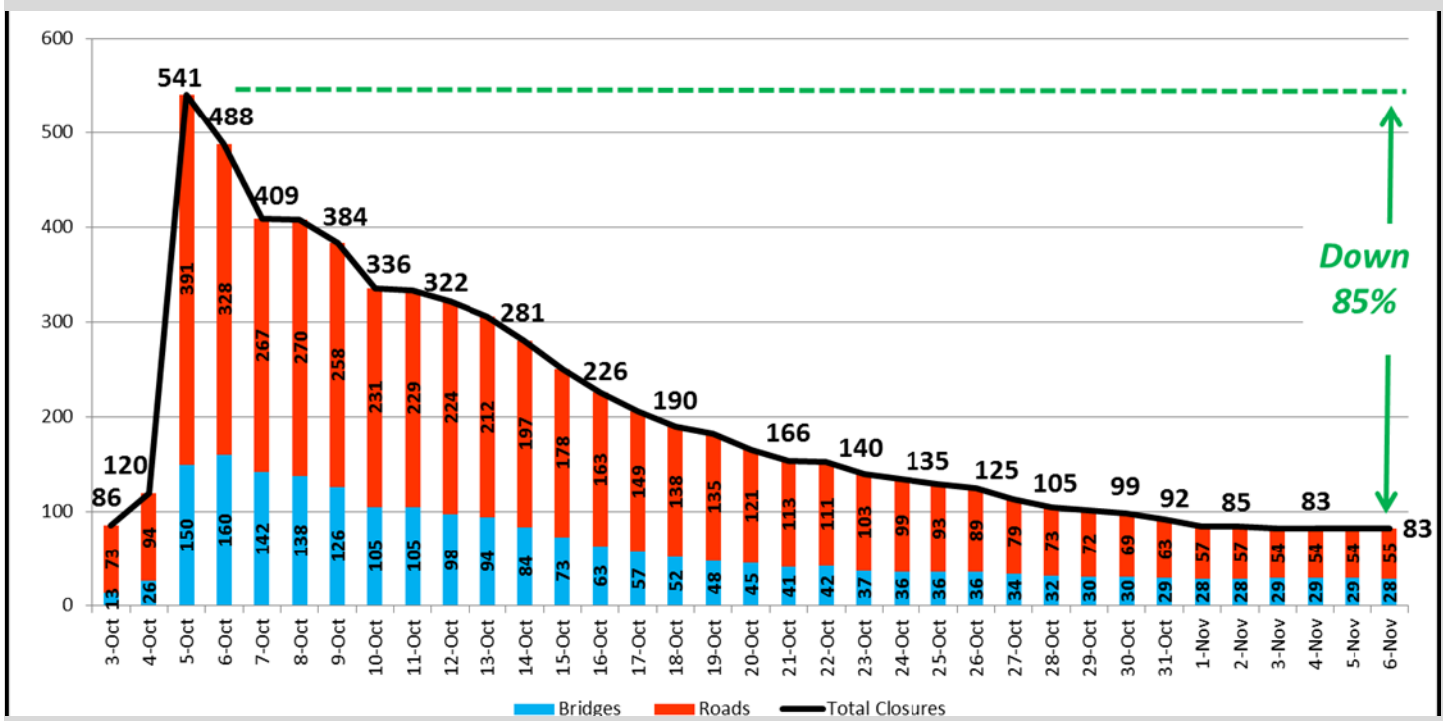

**10 Primary Routes remain CLOSED statewide:** Richland: US 21, SC 48 & SC 769. Clarendon: US 15, US 301 & US 521 (partial). Newberry: US 176. Florence: SC 51. Sumter: US 76 Business (partial). Williamsburg: SC 512.

26 of the remaining 85 closures are expected to be re-opened by Thanksgiving.

At least 16 of the remaining 29 bridge closures will require bridge replacements, major bridge repairs or major culvert replacements. Please see the Road Closure Report for a detailed listing,

26 routes have undetermined reopening dates due to dam failures. Please see the Road Closure Report for a detailed listing,




# Infrastructure Recovery Daily Report

Friday, November 6, 2015

All repairs to the state-maintained system have been completed in 14 Counties to date:

Abbeville County, Allendale County, Anderson County, Bamberg County, Berkeley County, Charleston County, Colleton County, Darlington County, Dorchester County, Greenwood County, Horry County, Laurens County, Marion County, and McCormick County.

## County by County Work Plan for the State-Maintained System

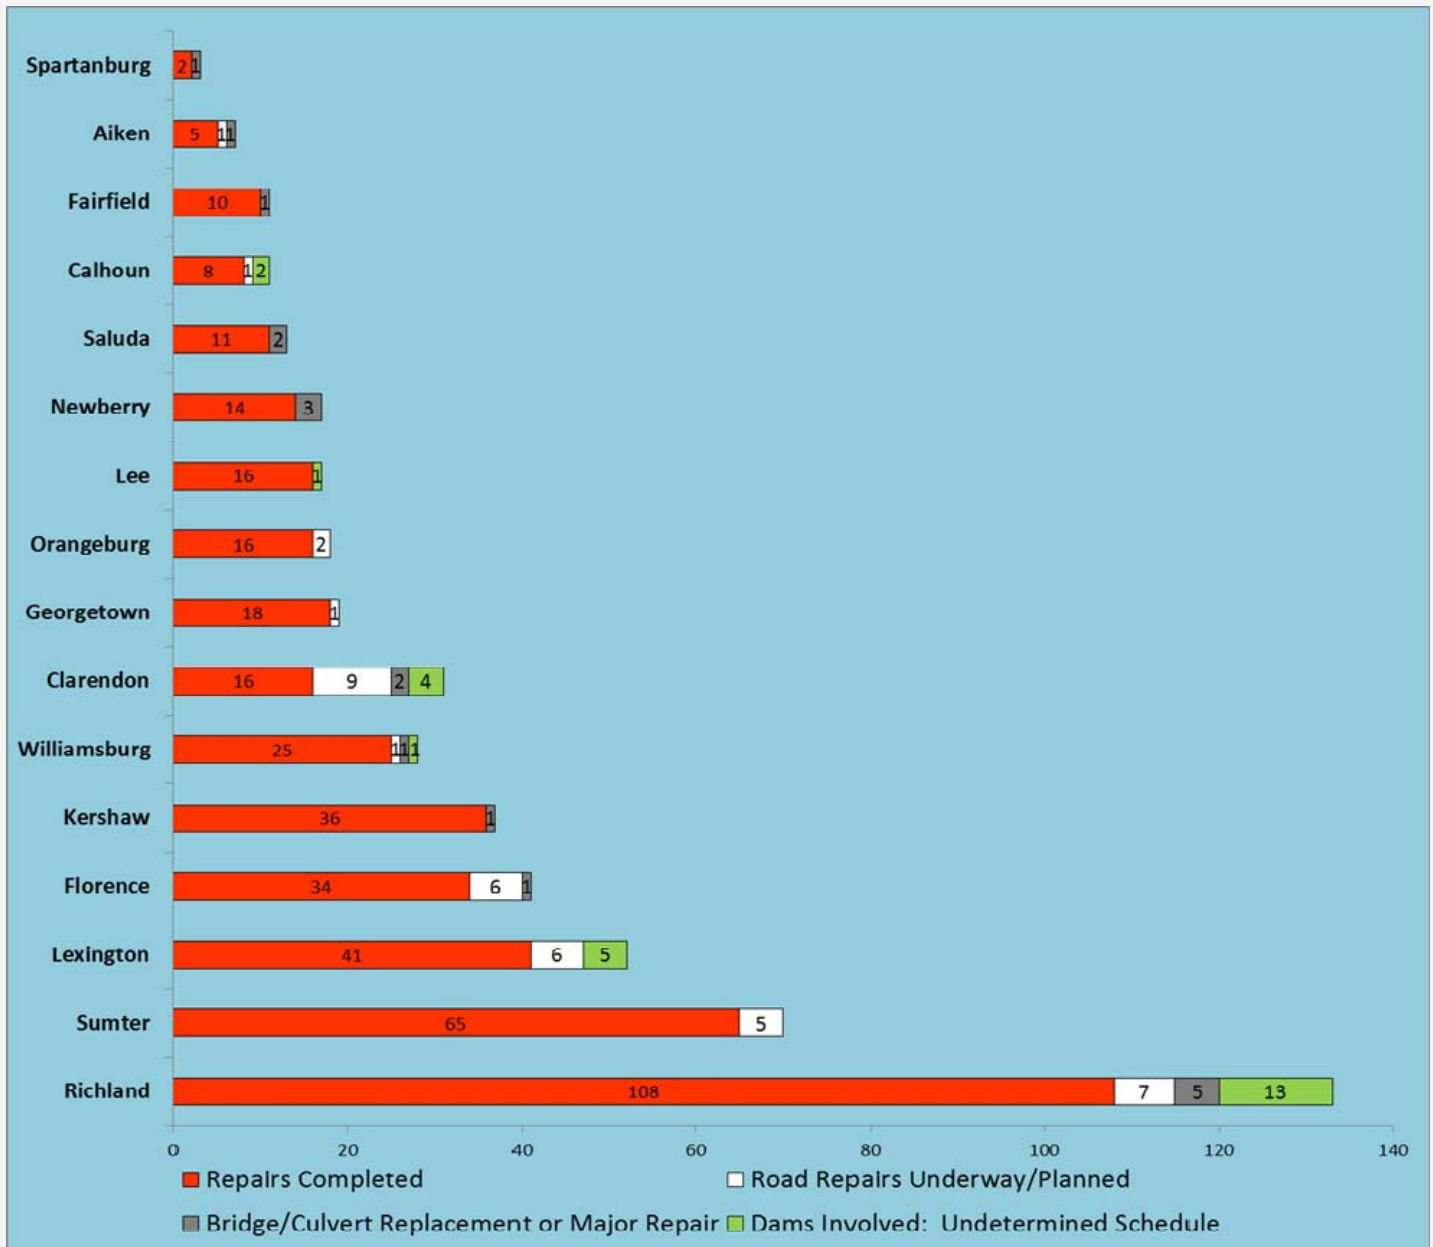

## Debris Removal Operations

Collected to Date: 1,311 loads (63,322 CY)

Please visit us at [www.scdot.org](http://www.scdot.org) for updated information. Updates are also provided on Facebook & Twitter.
